

## West Toronto Diamond – Delivery Alternatives

December 13, 2007



GO TRIP  
AGM PROGRAM MANAGERS



## CURRENT CSIF BUDGET \$ 77 million

- **Work completed to date – Design and Enabling Works**
  - **Committed cost to date: \$ 41.5 million**
  - **Spent to date: \$ 34.5 million**
  - **Balance is CN track work / detour and CA costs**
  - **CN detour is approximately \$1 million**
  
  - **For \$60 million we can construct the east pipe pile wall**
  
  - **NOTE: DECISION TO PROCEED WITH 2 OR 4 TRACK NEEDS TO BE MADE, AS 2 TRACK HAS A DEEPER CENTRE WALL**
    - Option 1 – if 4 track structure – start the west wall
    - Option 2 – if 2 track structure – detour, then start centre wall
- 



# Staging drawings



# TRACK CORRIDOR ALTERNATIVES: EAST WALL ONLY




# TRACK CORRIDOR ALTERNATIVES: PARTIAL PROJECT - TWO (2) TRACK CORRIDOR




# TRACK CORRIDOR ALTERNATIVES: FULL PROJECT - FOUR (4) TRACK CORRIDOR



# CURRENT PROJECT STATUS

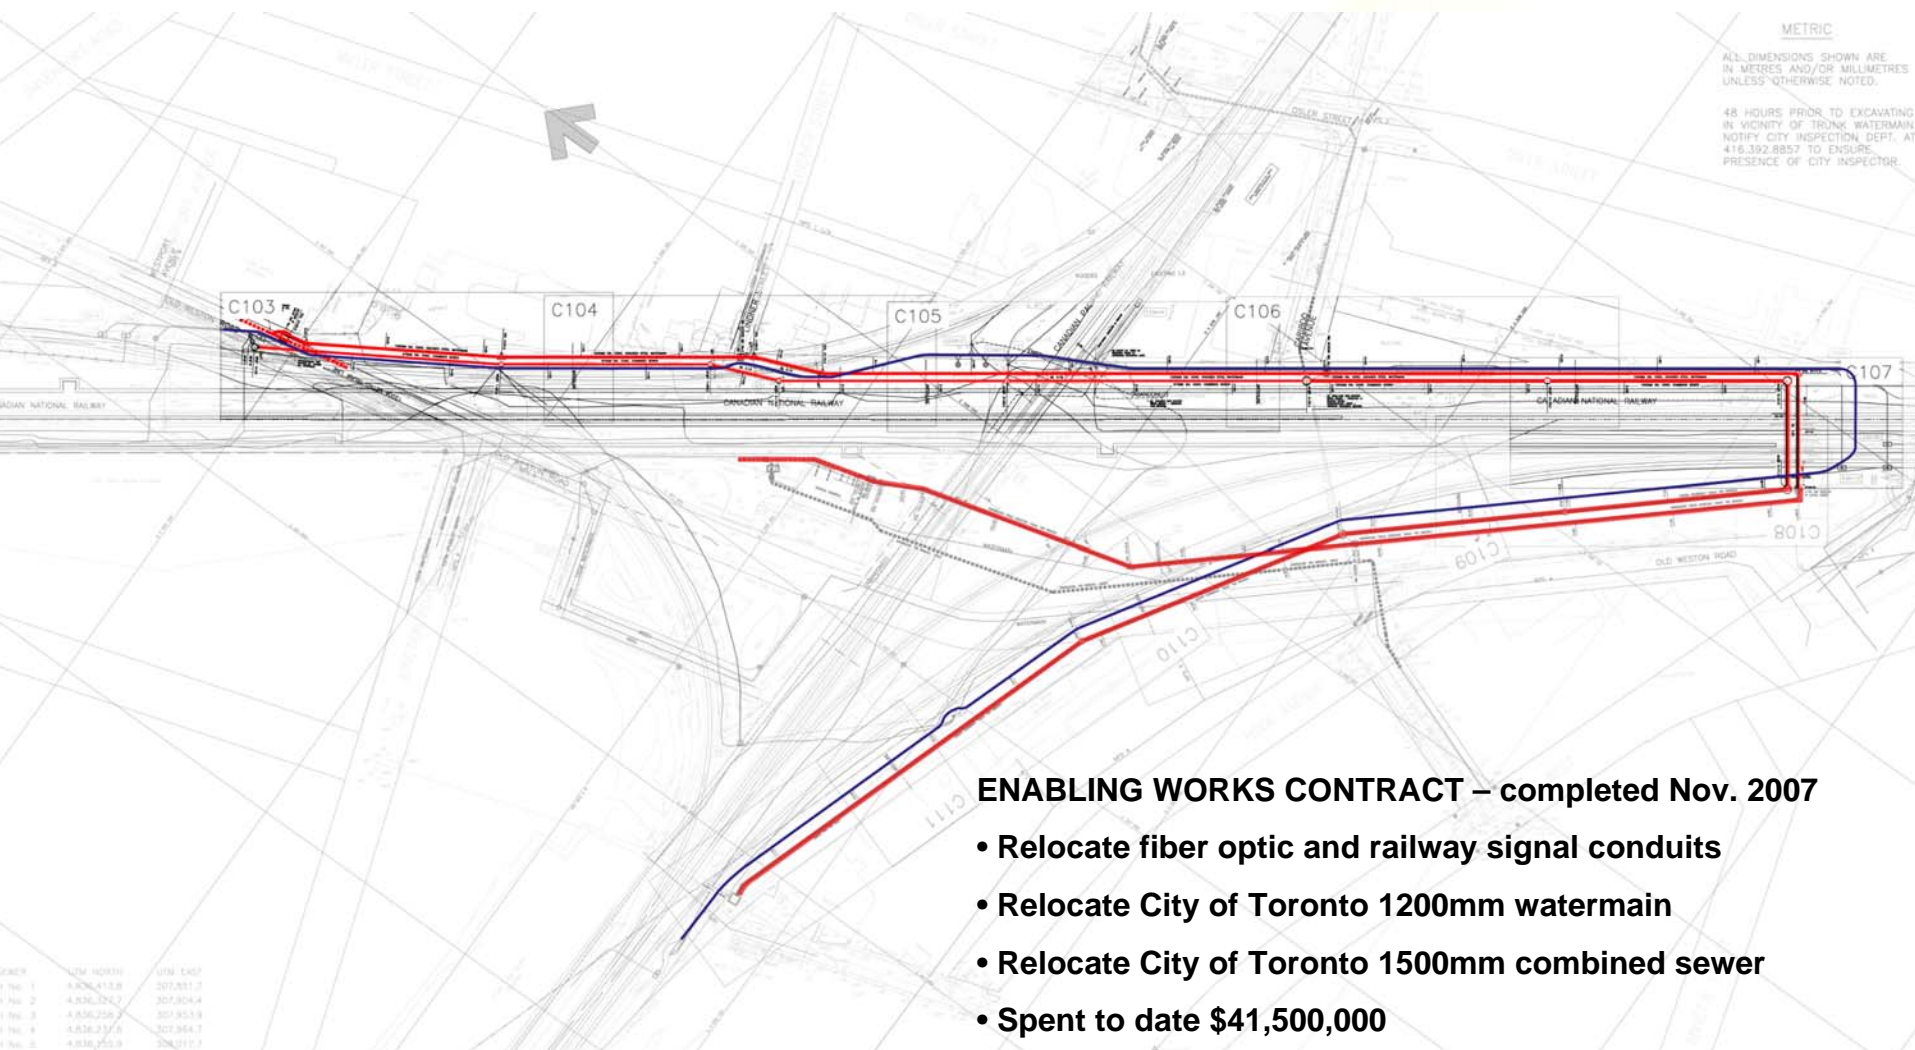


# 4-TRACK CORRIDOR – STAGE 1

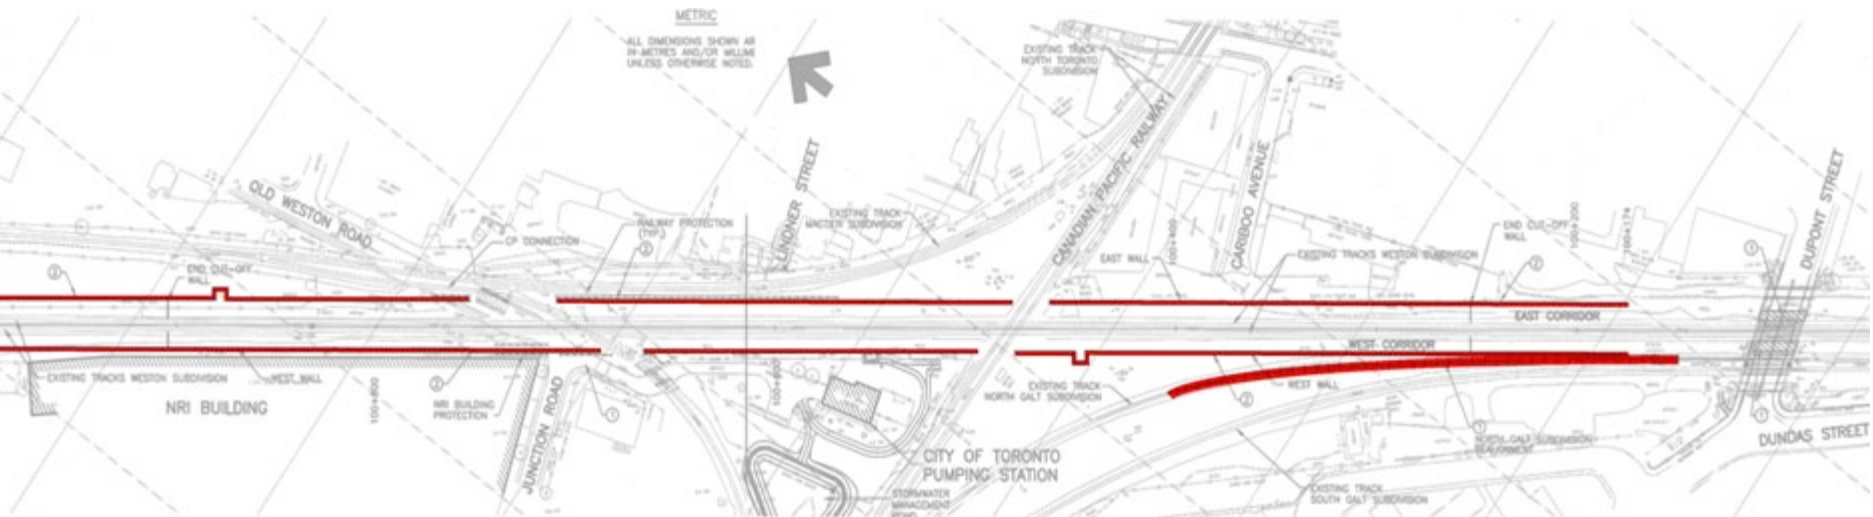

## STAGE 1:

- Construct east and west pipe pile walls
- Relocate portion of north Galt Subdivision

# 4-TRACK CORRIDOR – STAGE 2

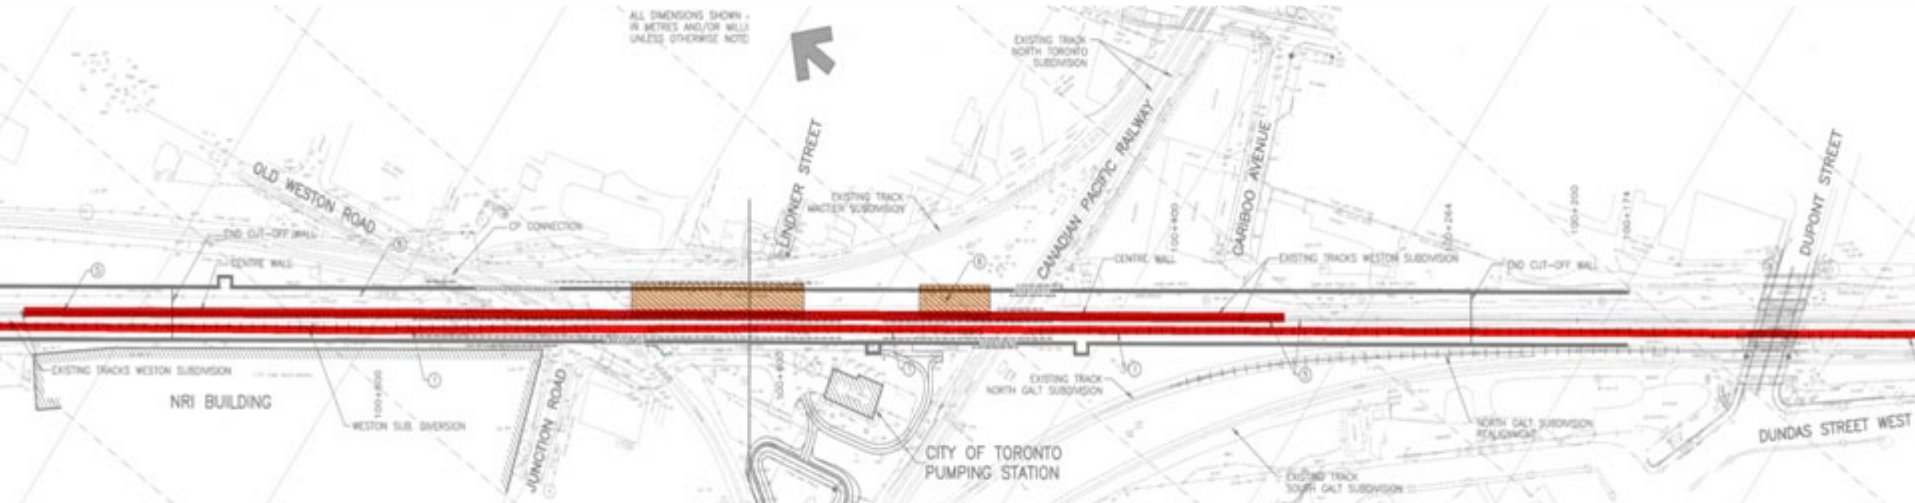


## STAGE 2:

- Construct Old Weston Road & CPR Bridges in preparation for sliding
- Construct CN Weston Sub detour track






# 4-TRACK CORRIDOR – STAGE 5

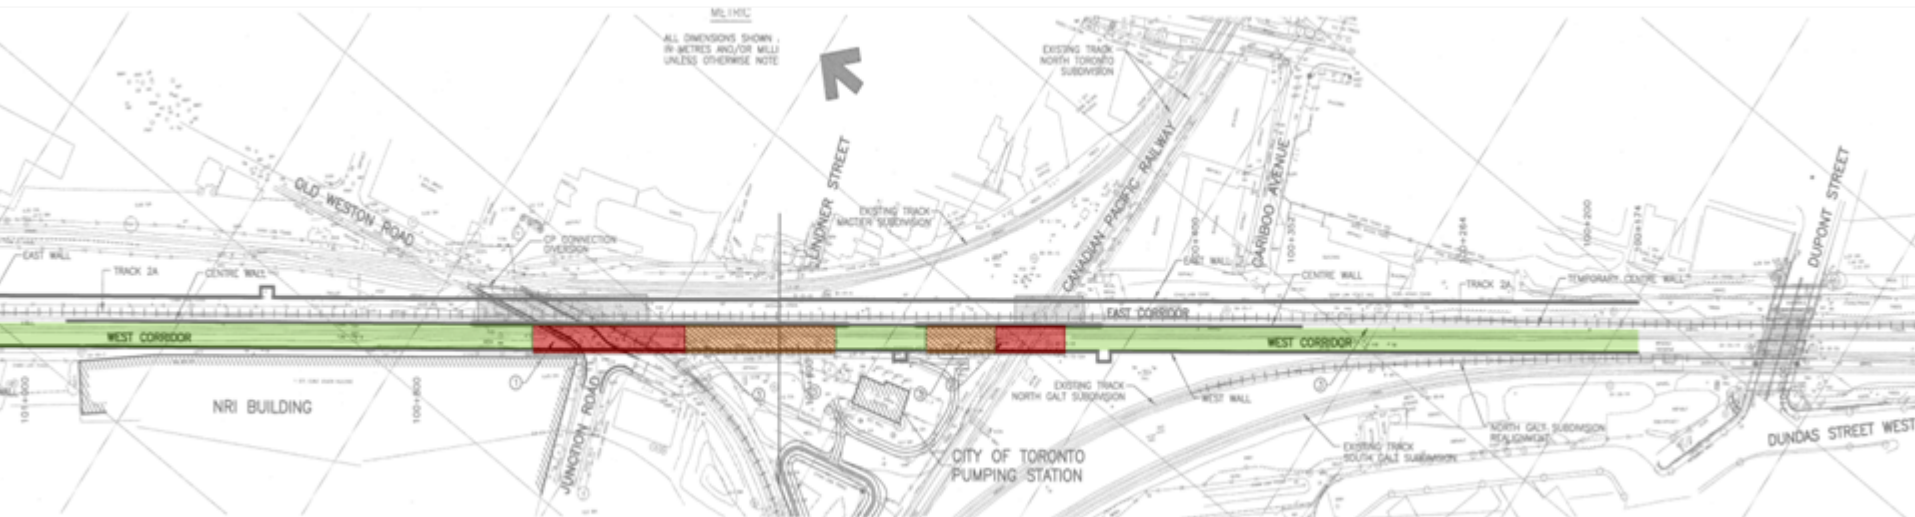

## STAGE 5:

- Slide Old Weston Rd. & CPR west corridor bridges into place
- Excavate west corridor


# 4-TRACK CORRIDOR – STAGE 6

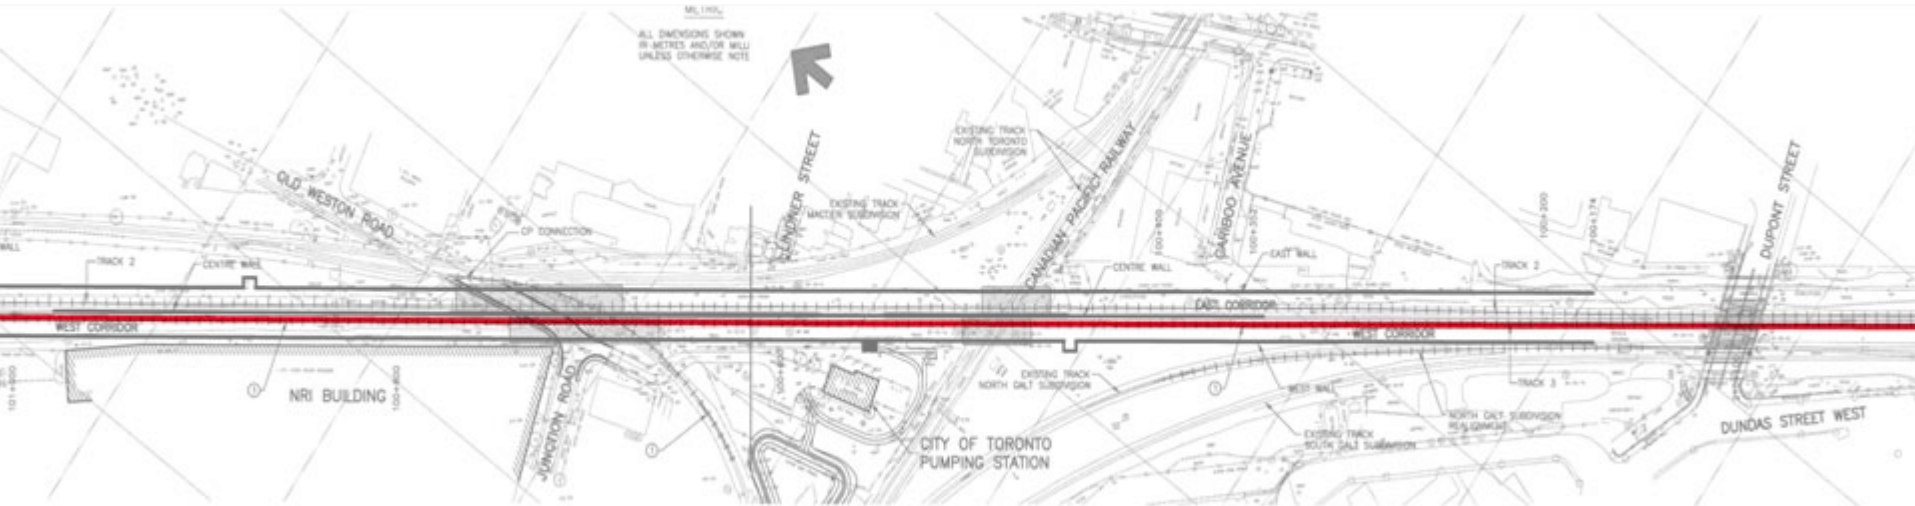

## STAGE 6:

- Construct CN Weston Sub tracks in west corridor
- Complete project May 2010
- Total project cost \$160,000,000

# 2-TRACK CORRIDOR – STAGE 1

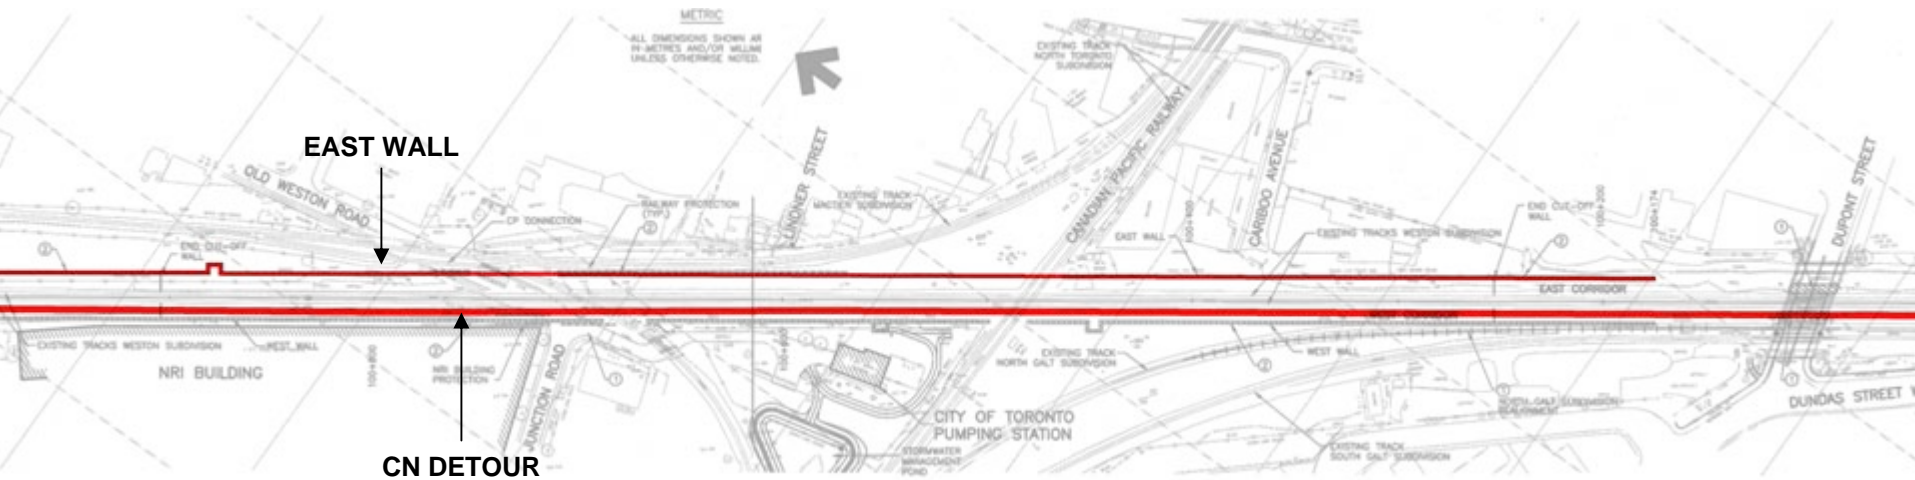


## STAGE 1:

- Construct East wall
- Construct CN detour



## 2-TRACK CORRIDOR – STAGE 3

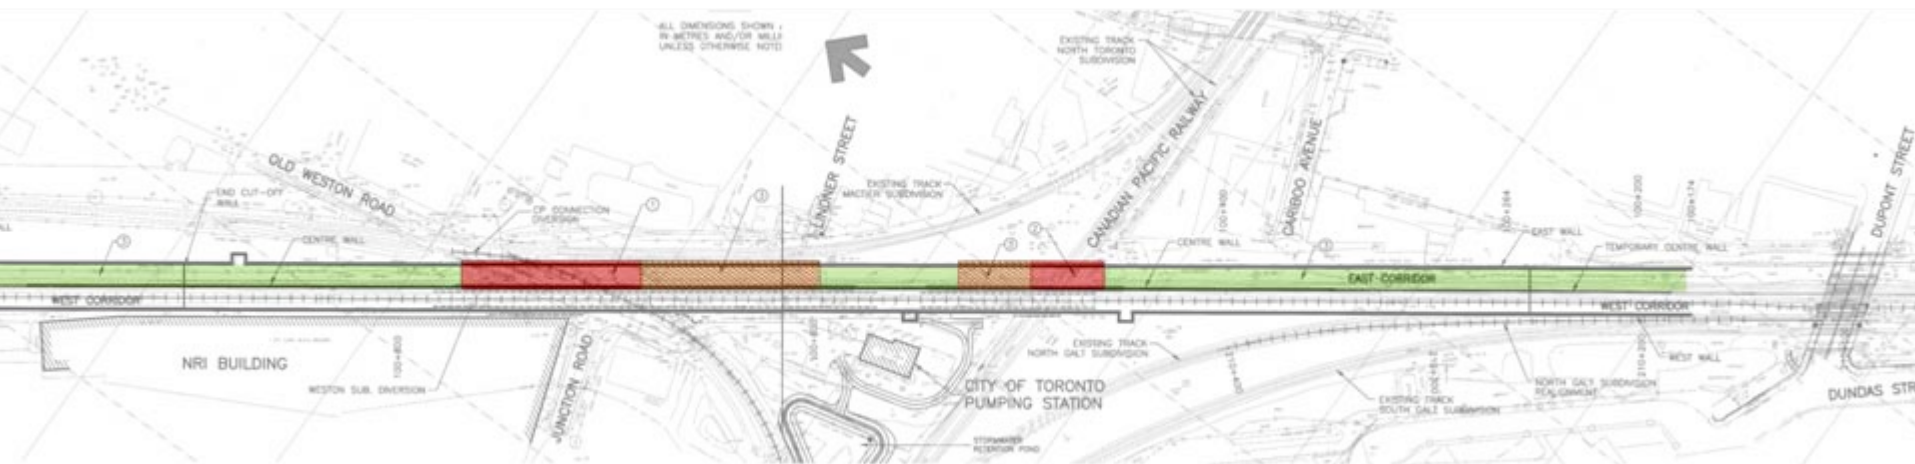

### STAGE 3:

- Slide Old Weston Rd. bridge & CPR bridge into place
- Total Project Cost \$95,000,000
